


BLANS Project Schedule Update

as of November 2010

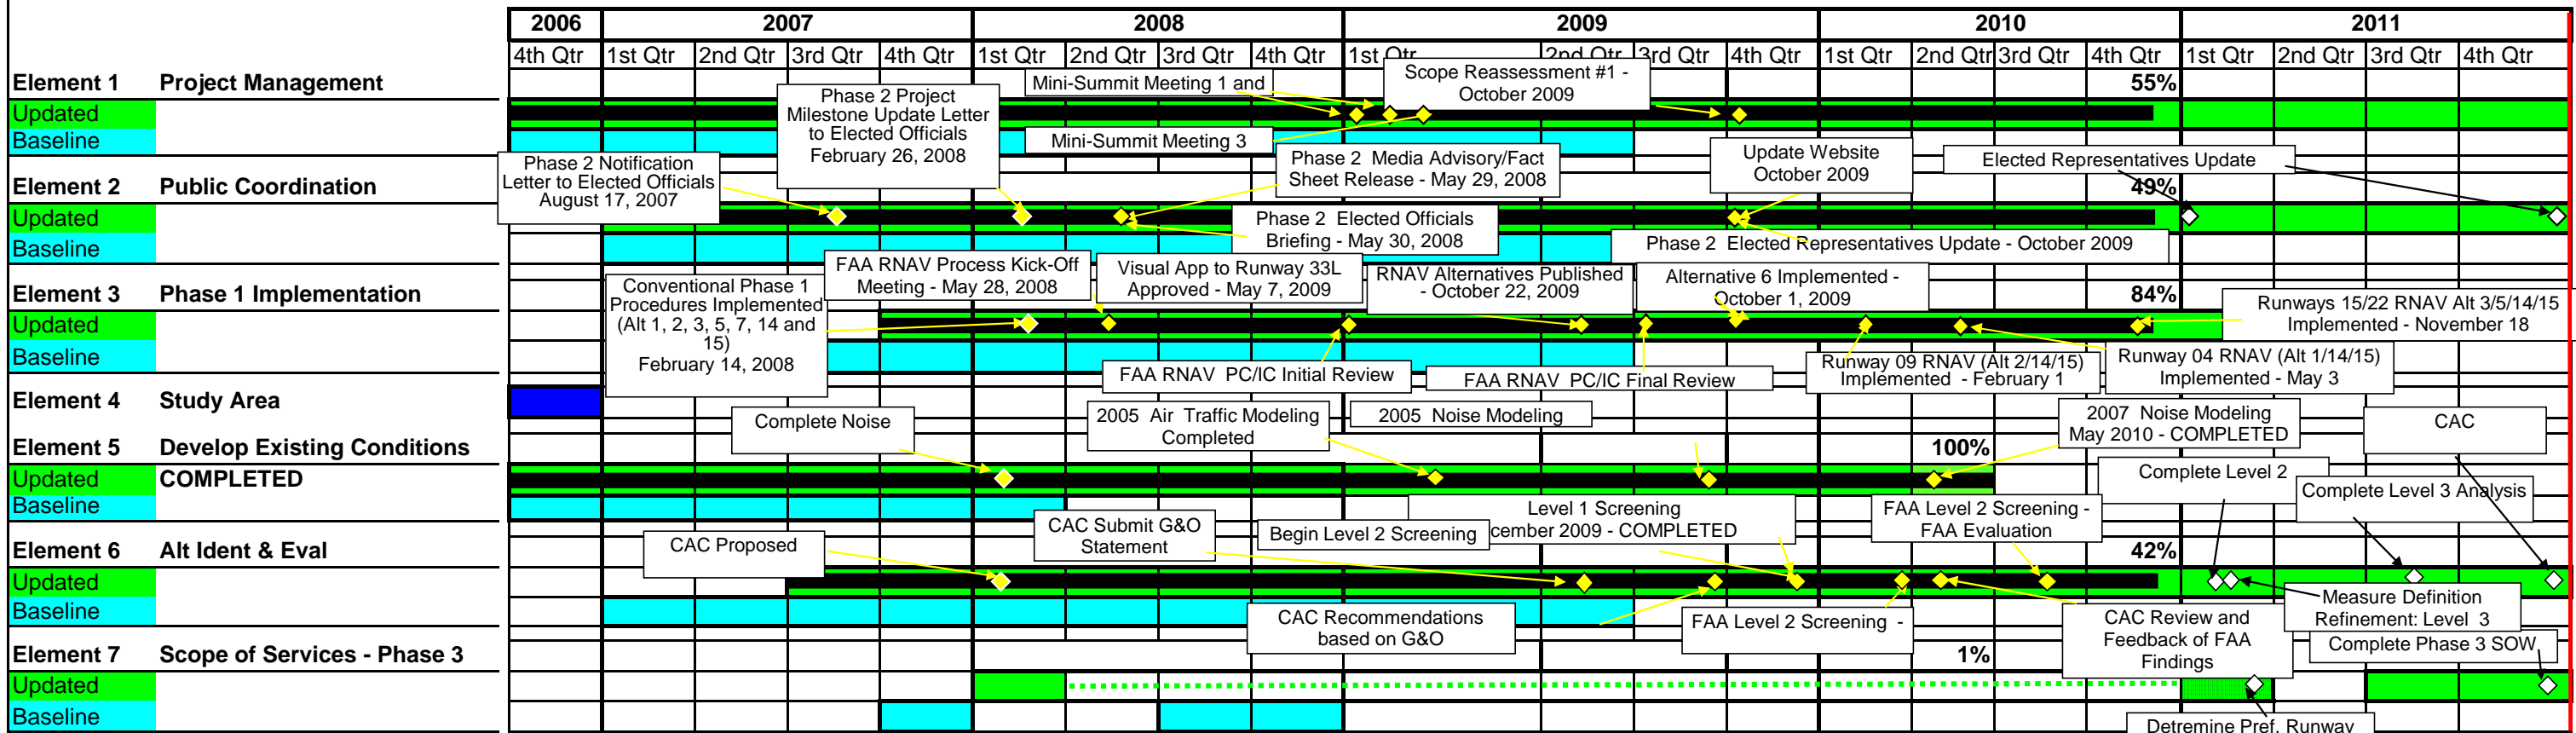

Legend

- Updated Timeline
- Baseline Timeline
- Completed
- Actual Progress
- Contract Expiration Date

Schedule Changes:

- ◆ Critical Path Milestone that is Delayed
- ◆ Milestone Completed: Completed Phase 1 Alternative Implementation
- ◇ Next Milestone: Complete Measure F-S Level 2 Assessment; Complete Level 2 Process; Refinement Efforts for Level 3; February 2011 BOS/TAC Meeting

Schedule Impact of Change

Determine Pref. Runway Advisory Program Intentions/Objectives

BLANS - Project Consultant Budget Status as of October 2010

Task

<u>No.</u>	<u>Description</u>	Project to Date	Budget (Reallocated 10/2009)	Percent
1	PROJECT MANAGEMENT	\$ 320,826.37	\$ 587,199.00	55%
2	PUBLIC COORD	\$ 255,769.51	\$ 526,105.00	49%
3	PHASE 1 IMPLEMENTATION	\$ 73,514.00	\$ 87,060.00	84%
4	STUDY AREA	\$ -	\$ -	N/A
5	EXISTING CONDITIONS	\$ 1,069,842.36	\$ 1,069,842.36	100%
6	ALTERNATIVES ID/EVAL	\$ 557,548.27	\$ 1,312,231.64	42%
7	SCOPE OF SERVICES-Phase 3	\$ 1,176.00	\$ 107,911.00	1%
TOTAL		\$ 2,278,676.51	\$ 3,690,328.00	62%
